



Town of Chatham

Office of the Select Board
Town Manager
549 Main Street
Chatham, MA 02633



Jill R. Goldsmith
TOWN MANAGER
jgoldsmith@chatham-ma.gov

Tel: (508) 945-5105
Fax: (508) 945-3550
www.chatham-ma.gov

NEWS RELEASE

FOR IMMEDIATE RELEASE – September 13, 2024

Contact: Robert Faley
Director of Public Works
(508) 945-5155; rfaley@chatham-ma.gov

Sewer Construction Update

Chatham – C.C. Construction, Inc. will be continuing work for the Phase 1D-2A: Route 137 – Morton Road Sewer Extension Project (1D-2A) and the Queen Anne Pumping Station (QAPS) Upgrade. Dig It Construction LLC will be continuing work on the Phase 1E-2 – Stage Harbor Road Sewer Extension Project (1E-2).

Robert B. Our Co., Inc. will be commencing work on the Mill Pond Pumping Station Upgrade (MPPS) and C.C. Construction, Inc. will be commencing work on the Phase 1C-5 – Oyster Pond Sewer Extension (1C-5) later this month.

Work for the week of September 16th – 20th:

1D-2A:

- Continued site work at Pump Station #3 (Meetinghouse Road) and Pump Station #4 (Twine Field Drive) is expected.

QAPS:

- Continued site work at the pump station site is expected (40 Queen Anne Road; south side of Queen Anne Road and Oyster Pond Furlong intersection). ***For public safety reasons, the southbound lane of Queen Anne Road will be closed from Chatham Village Market to the Oyster Pond Furlong intersection. Local traffic only but access may be limited depending on the construction. Police details and signage will be in place.***

1E-2:

- Continued site work is expected at the pumping station site (Old Mill Boat Yard/Harbormasters Garage) and continued sewer work on Stage Harbor Road (sewer lateral) and Honeysuckle Lane (gravity sewer and sewer lateral). ***For public safety reasons, the road will be closed from***

Honeysuckle Lane to Bridge Street. Local traffic only but access may be limited depending on construction. Police details and signage will be in place. Detour will be as follows:

- ***Detour from Champlain Road – via Bridge Street***
- ***Detour from Bridge Street around Champlain Road***
- ***From Stage Harbor Road – via Cedar Street to Champlain Road***
- ***See figures below for additional information for WORK ZONE 2***

MPPS:

- No work planned. Schedule pending.

1C-5:

- Commence construction at the Independence Lane Pump Station site and continue to work east on Independence Lane to the intersection with Stage Harbor Road. Construction on Independence Lane is expected to continue through mid-October. ***Starting SEPTEMBER 16, 2024, to avoid being inconvenienced during the daytime you will be required to move your vehicles off Independence Lane before 7:00AM. The Chatham Police Department will be on site daily to assist you finding alternate parking. Contractor hours are typically from 7:00 AM to 5:00 PM, weather depending. No work is scheduled for nights, weekends, or holidays. Work may be extended to 7 PM under special circumstances.***

Two Week Look Ahead (9/23– 9/27):

1D-2A:

- Continued site work at Pump Station #3 (Meetinghouse Road) and Pump Station #4 (Twine Field Drive) is expected.

QAPS:

- Continued site work at the pump station site is expected (40 Queen Anne Road; south side of Queen Anne Road and Oyster Pond Furlong intersection). ***For public safety reasons, the southbound lane of Queen Anne Road will be closed from the Chatham Village Market to the Oyster Pond Furlong intersection. Local traffic only but access may be limited depending on the construction. Police details and signage will be in place.***

1E-2:

- Continued site work is expected at the pumping station site (Old Mill Boat Yard/Harbormasters Garage).

MPPS:

- No work planned. Schedule pending.

1C-5:

- Continued construction at the Independence Lane Pump Station site and Independence Lane. Construction on Independence Lane is expected to continue through mid-October. ***Starting SEPTEMBER 16, 2024, to avoid being inconvenienced during the daytime you will be required to move your vehicles off Independence Lane before 7:00AM. The Chatham Police Department will be on site daily to assist you finding alternate parking. Contractor hours are typically from 7:00 AM to 5:00 PM, weather depending. No work is scheduled for nights, weekends, or holidays. Work may be extended to 7 PM under special circumstances.***

Three Week Look Ahead (9/30 – 10/4):

1D-2A:

- Continued site work at Pump Station #3 (Meetinghouse Road) and Pump Station #4 (Twine Field Drive) expected.

QAPS:

- Continued site work at the pump station site is expected (40 Queen Anne Road; south side of Queen Anne Road and Oyster Pond Furlong intersection).

1E-2:

- Continued site work is expected at the pumping station site (Old Mill Boat Yard/Harbormasters Garage).



MPPS:

- No work planned. Schedule pending.

1C-5:

- Continued construction at the Independence Lane Pump Station site and Independence Lane. Construction on Independence Lane is expected to continue through mid-October. ***Starting SEPTEMBER 16, 2024, to avoid being inconvenienced during the daytime you will be required to move your vehicles off Independence Lane before 7:00AM. The Chatham Police Department will be on site daily to assist you finding alternate parking. Contractor hours are typically from 7:00 AM to 5:00 PM, weather depending. No work is scheduled for nights, weekends, or holidays. Work may be extended to 7 PM under special circumstances.***

*****Please note that work associated with the Mill Pond Pumping Station is expected to affect access to the Town Landing beginning late-September. Additional information will be provided by the Harbormaster to all permit holders as the Contractor's schedule is confirmed for this area.*****

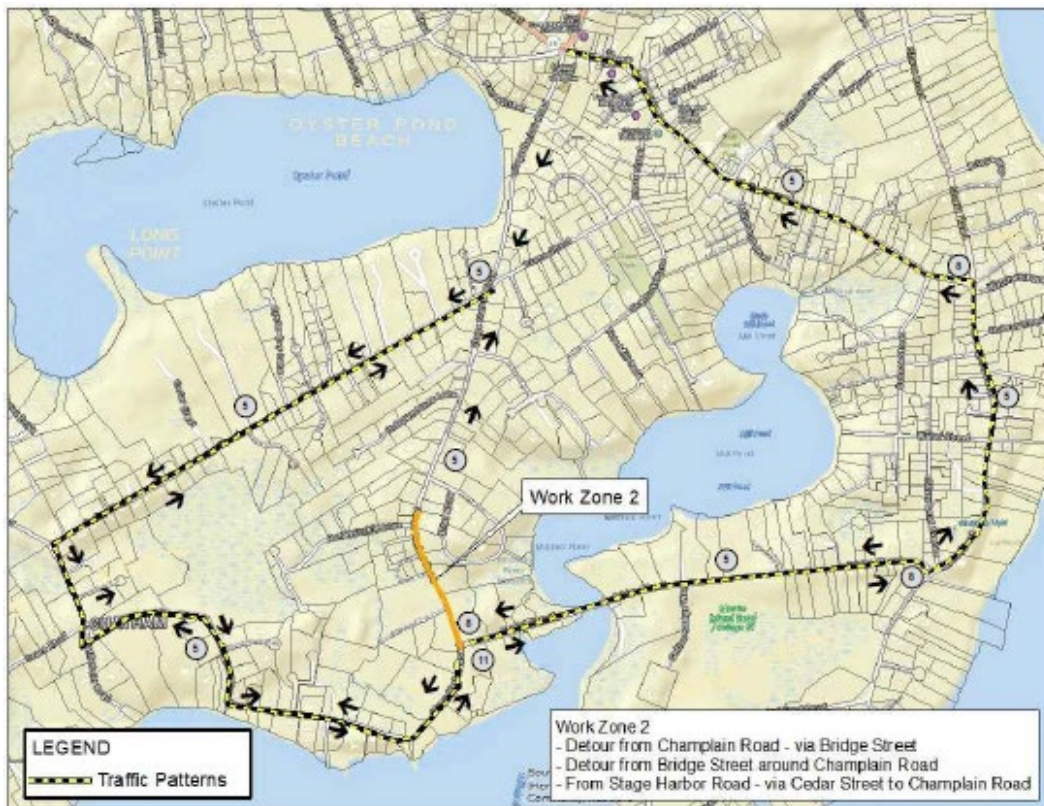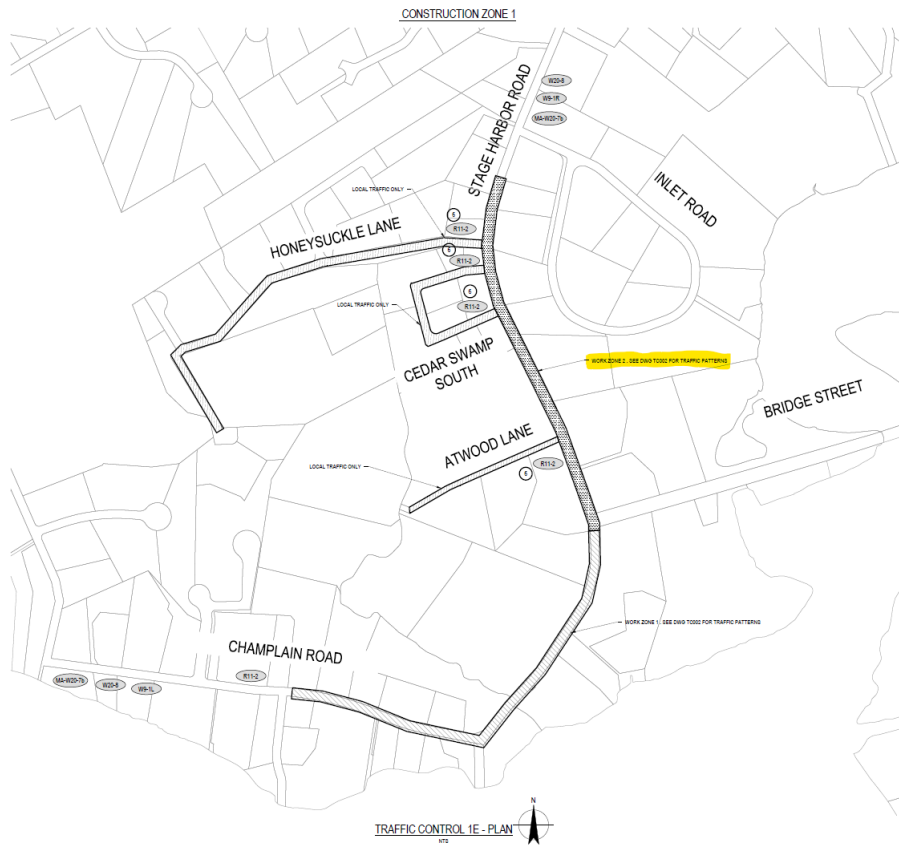

WORK ZONE 2 DETOURS - PLAN
NTS

Please note that this is a projected schedule and will be adjusted accordingly based on the Contractor's actual progress and the weather.

Roads will be passable at the end of each day. Police Details and Contractors will work with residents to ensure their needs for access are addressed.

Police Details and signage will be in-place to assist motorists in reaching their destination.

Normal work hours are 7:00 AM to 4:00 PM Monday to Friday, weather permitting, unless otherwise noted.

Sewer construction updates are being posted to the Town's website under the "Projects" icon as the primary information site for residents at <http://www.chatham-ma.gov>. We encourage you to visit for additional information regarding the CWMP and other important projects and events in Town.

Thank you for your patience and cooperation during this important project to restore and protect our environment.

###
